


Dredging and validation progress along canal

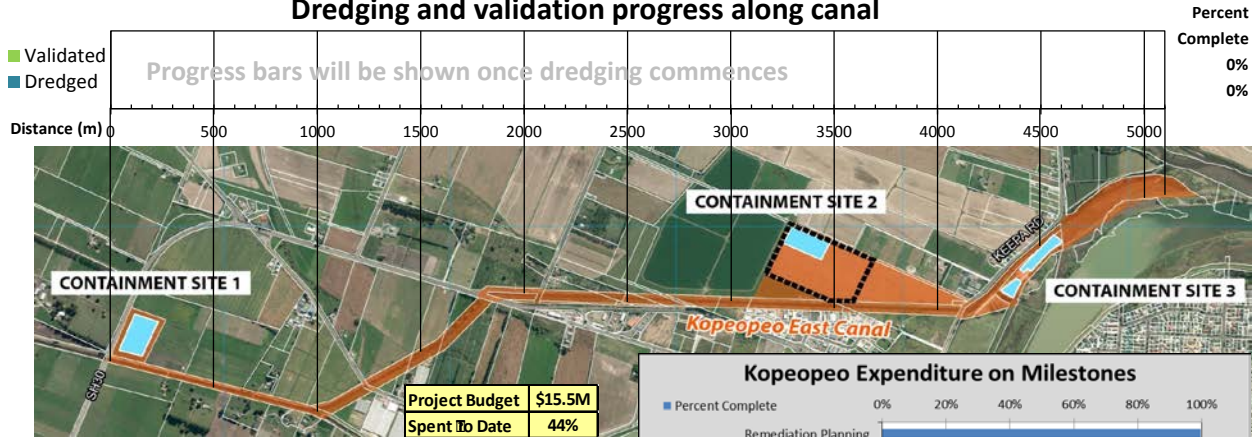

Percent Complete
0%
0%

KEY PROGRESS (past period)

- Preliminary works underway: erosion and sediment controls; topsoil removal; site access construction; culvert installation
- Traffic Management Plan revised in response to community feedback
- Flood Management Plan drafted
- CS1 fencing completed
- Sheetpile arrived in Whakatāne and stacked on canal bank at control structure locations
- Eel trial – removal and sampling completed
- New groundwater wells installed at CS1
- Groundwater wells decommissioned at CS2

ISSUES ARISING & BEING ADDRESSED

- Excavator overturned on canal bank when offloading. No injuries. Pollution Prevention attended - small hydraulic oil spill contained – investigations being undertaken by Contractor to establish cause, including BOPRC and Worksafe
- Power outage around Shaw Road being investigated by Contractor following delivery of sheetpile to Kope Canal Road
- Community Monitor role is being established

ENVIRONMENTAL MONITORING (to be finalised in EMVP)

Indicator	Comment
Air Quality	Background monitoring underway
Water Quality	Background monitoring underway
Groundwater	Background monitoring underway
Other monitoring	TBD
Other monitoring	TBD

COMPLIANCE MONITORING

Consent Compliance	Compliant with all consent conditions to date
Trigger level deviations	None
Water Abstraction	0 m3
0 complaints received	

MONITORING REPORTS

COMPLIANCE OFFICERS

- Reviewed and approved Noise Management Plan, Erosion and Sediment Control Plan, and revised Traffic Management Plan


INDEPENDENT MONITOR

- Received Dredge Management Plan for review
- Reviewed Traffic Management Plan and Environmental Monitoring and Validation Plan and presented comments on both at CLG
- Independent Monitor Field Officer attended eel removal trial and excavator incident and provided feedback

CULTURAL MONITOR

- Provided overview of CM involvement and expectations to Contractors at CS1 toolbox meeting
- Observed eel trial and provided support to freshwater ecologist
- Discovery Protocol updated for physical works and dredging

Kopepeo Expenditure on Milestones

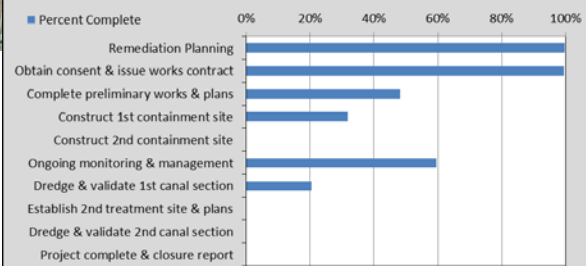

PLANNED (upcoming period)

- CS1 construction continues
- Gate at north of CS1 for emergency exit
- Pipeline route planning
- Finalisation of FMP and flood control structure design

HEALTH & SAFETY

Item	No#	Comment - Actions - Outcome
Inductions	31	to date
Safety Contacts	3	Check pump test and tag Watch traffic on road during induction Install hazard ID board at site entrance
Near Hits	1	excavator roll over
First Aid	0	
Medical Treatment Injury	0	
Lost Time	0	
Environmental	2	Hydraulic oil spill into canal Dust monitor offline temporarily
Progress - Meters		Currently not applicable
General		Planning going well

PROJECT REPORTS

COMMUNITY LIAISON GROUP

- CLG Newsletter sent
- CLG meeting held on 16 May
- CLG recommended Community Monitor role
- Communication and Engagement Plan update progressing

ENGINEER TO CONTRACT

- Chaired 5 contract meetings
- Reviewed design, quantities and prices for CS1
- Received 5 progress claims and issued 5 payment schedules
- Received 46 Notices to Engineer to date
- Issued 28 Notices to Contractor to date

PRINCIPAL WORKS CONTRACTOR

- Coordinated preliminary works and eel trial
- Coordinated installation of new groundwater wells at CS1
- Coordinated transportation of sheetpile to site
- Coordinating sheetpile installation and control structure design

PROJECT MANAGER

- Coordinating review of management plans
- Scoping relocation of bioremediation trial bags to CS1
- Initial planning and enabling works for bioremediation in-situ trial
- Coordinating baseline eel sampling
- Terminated lease of land formerly planned for CS2
