


Dredging and validation progress along canal

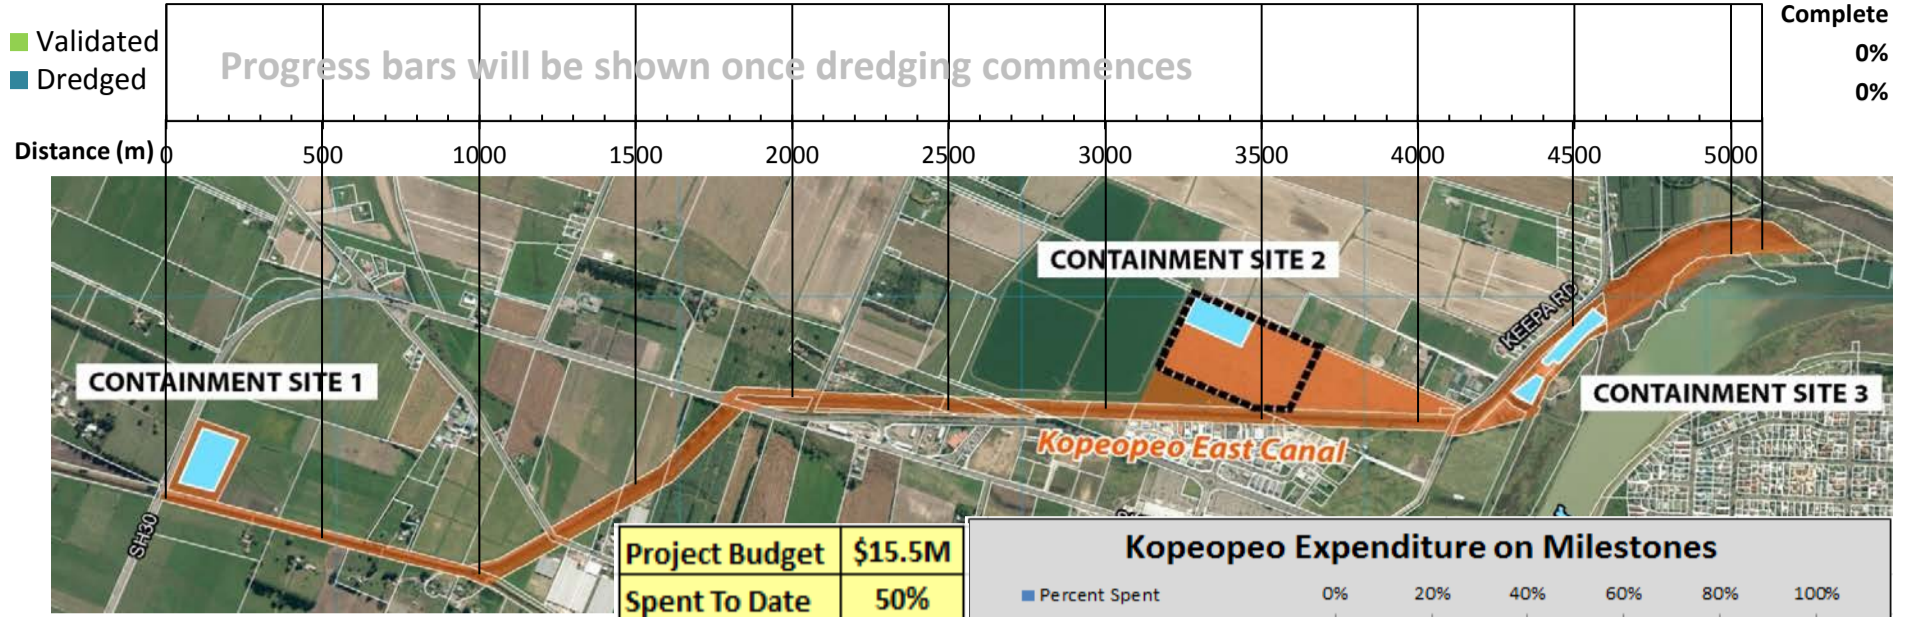

Percent Complete
0%
0%

- KEY PROGRESS (past period)**
- Completed construction of perimeter bund base
 - Completed construction of internal haul road for truck access
 - Flood Management Plan completed and submitted for peer review
 - Preliminary works progressing: erosion and sediment controls; topsoil removal; site access construction; culvert installation

- PLANNED (upcoming period)**
- Install gate at north of CS1 for emergency exit
 - Plan and establish pipeline route
 - Finalise control structure design
 - Initiate FMP peripheral works consultation
 - Place bags and liner on CS1
 - Remove vegetation from along canal
 - Create tree planting plan
 - Supply power to CS1
 - Finalise outstanding management plans

ENVIRONMENTAL MONITORING (to be finalised in EMVP)


Indicator	Comment
Air Quality	Background monitoring underway
Water Quality	Background monitoring underway
Groundwater	Background monitoring underway
Other monitoring	TBD
Other monitoring	TBD

COMPLIANCE MONITORING

Consent Compliance	Compliant with all consent conditions to date
Trigger level deviations	None
Water Abstraction	0 m3
0 complaints received	

- ISSUES ARISING & BEING ADDRESSED**
- Continuing adverse weather impacting CS1 construction
 - Investigations of excavator overturn incident complete
 - Investigation of Shaw Road power outage was inconclusive
 - Heavy rain in late June caused potential non-compliance of stormwater monitoring

- MONITORING REPORTS**
- COMPLIANCE OFFICERS**
- Gave Engineer's Representative advice on removing trees from along canal near CS3
 - Required minor improvements to earthworks sediment control and fuel management at CS1
- INDEPENDENT MONITOR**
- Issued first monthly report to CLG
 - Daily site inspections carried out
- CULTURAL MONITOR**
- Met with Project Team to discuss cultural monitoring support needs

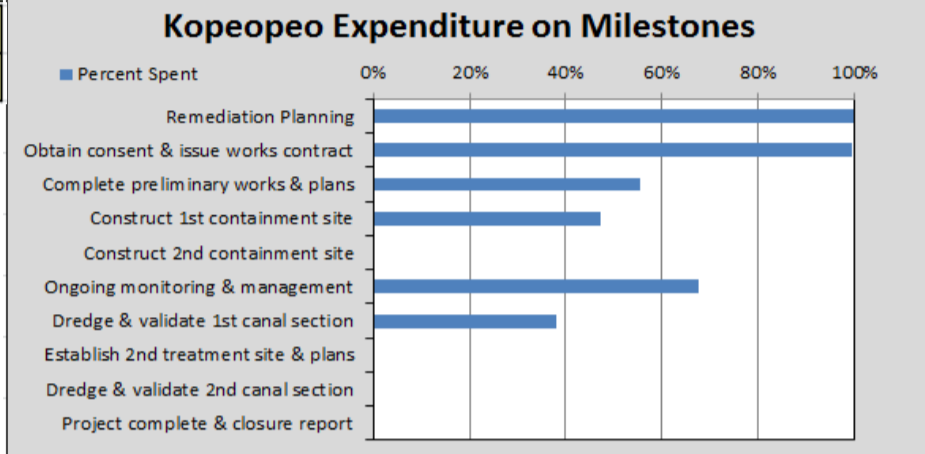

HEALTH & SAFETY

Item	No#	Comment - Actions - Outcome
Inductions	53	to date
Safety Contacts	3	
Near Hits	0	
First Aid	0	
Medical Treatment Injury	0	
Lost Time	0	
Environmental	1	Stormwater discharged following heavy rain (71mm) potentially non-compliant
		Modifications to Silt-buster completed
		Repairs carried out on silt fence
		Dust monitor back online
Progress - Meters		Currently not applicable
General		Planning going well

- PROJECT REPORTS**
- COMMUNITY LIAISON GROUP**
- Community Liaison Group meeting held on 20 June
 - Tech Talk on Flood Management presented to CLG
 - Community Monitor appointed by CLG
 - Communication and Engagement Plan (CEP) update progressing
- ENGINEER TO CONTRACT**
- Chaired six site meetings to date
 - Received six progress claims and issued six payment schedules
 - Received 47 Notices to Engineer
 - Issued 30 Notices to Contractor
- PRINCIPAL WORKS CONTRACTOR**
- Progressing preliminary works as described in 'Key Progress'
 - Coordinating finalisation of control structure design
 - Pipe line delivered and establishing welding equipment ready for progressing installation phase
 - Established parking area next to CS1
 - Drained and cleaned out HB50 Siltbuster at CS1
 - Established second access way into CS1 support area
 - Repaired soft areas of support zone
- PROJECT MANAGER**
- Completed site safety audit at CS1
 - Coordinating finalisation and alignment of Dredge Management Plan and Flood Management Plan
 - Coordinating baseline eel sampling
 - Formalising Community Monitor role
 - Analysing weather-related impacts on project
